

County/Twp: WAYNE Co / Rompton Boro

SECTION 9106 OF THE PENNSYLVANIA VEHICLE CODE

Date: Oct 14, 2014

DIRT AND GRAVEL ROADS GRANT APPLICATION

<u>Prompton Boro</u>	<u>P.O. Box 13</u>	<u>Prompton PA</u>	<u>18456</u>
Official Name of Applying Agency	Mailing Address	Post Office Box	Zip Code
<u>Kirk Fries</u>	<u>570-253-1740</u>	<u>NA</u>	<u>wirenut@echoes.net</u>
Contact Person	Phone	FAX	E-Mail
<u>Van Aken Creek</u>	<u>Balsam Swamp Road</u>	<u>Road ID Number / Name</u>	
Affected Stream or Tributary			



1. List personnel who have received "Environmentally Sensitive Maintenance of Dirt and Gravel Roads" Training.

<u>Kirk Fries / Conc. Mem</u>	<u>2014</u>	<u>Name / Position</u>	<u>Year</u>
Name / Position	Year	Name / Position	Year

2. Will the work involve floodplains, stream crossings, stream work or wetlands? Yes X No

3. ☐ Eroded ditches	☐ Inadequate stream crossings	☒ Lack of road crown	☐ Other
☐ Eroded road banks	☐ Inadequate cross pipes	☒ Poor base composition	
☒ Discharges directly to stream	☐ Groundwater in road bed	☐ Excessive road shading	
☐ Stream bank erosion	☐ Excessive loss of road fines (dust)	☐ Ineffective vegetative buffers	

4. Is this a previously verified work site? Yes No If yes list the circled number from the map. NA

5. Do materials proposed to be used on the project meet State Conservation Commission conditions for non-polluting? Yes X NA

List commercial products to be used for the project.

6. On the back of the application include a sketch of the road with the proposed work elements. Include a photocopy of the topographic map with the work site highlighted.


7. Proposed start/ completion date: 6-2015 / 8-2015 Check if project would be considered an emergency:

8. Project cost summary:

Project Expenditures		In Kind Contributions	
Materials	Equipment	Materials	Equipment
<u>Contractor Supplied Estimate</u>		<u>Grant Requested</u>	
① <u>RESURFACE ROAD, CLEAN BANK & CREATE DITCHLINE & INSTALL R.4 STONE.</u>		① <u>CLEAN TREES & REMOVE GROWTH OF PIPE CROSSING ON BANK TO BE RESHAPED</u>	
<u>LABOR & EQUIP:</u>		<u>LABOR:</u>	<u>200-</u>
<u>MATERIAL:</u>		<u>EQUIP:</u>	<u>300-</u>
		<u>DIKER TIRE (10 hrs) (35/hr)</u>	<u>350-</u>
② <u>RESURFACE ROADWAY 14' WIDE WITH 8" LOOSE COMPACTED TO 6" DSA (1380' TOTAL DISTANCE)</u>		② <u>CREATE THROUGH BANK DRAINAGE ALIENS</u>	
<u>LABOR, EQUIP, MATERIAL -</u>		<u>LABOR:</u>	<u>100-</u>
		<u>EQUIP:</u>	<u>150-</u>
		<u>DIKER TIRE (3 hrs) (35/hr)</u>	<u>105-</u>
		<u>Total Project Value</u>	<u>\$ 1,205-</u>
		<u>In-kind Contributions</u>	<u>\$ 1,205-</u>
		<u>Applicant Signature</u>	<u> </u>

Rec'd 10/17/14 Not

PROJECT SKETCH

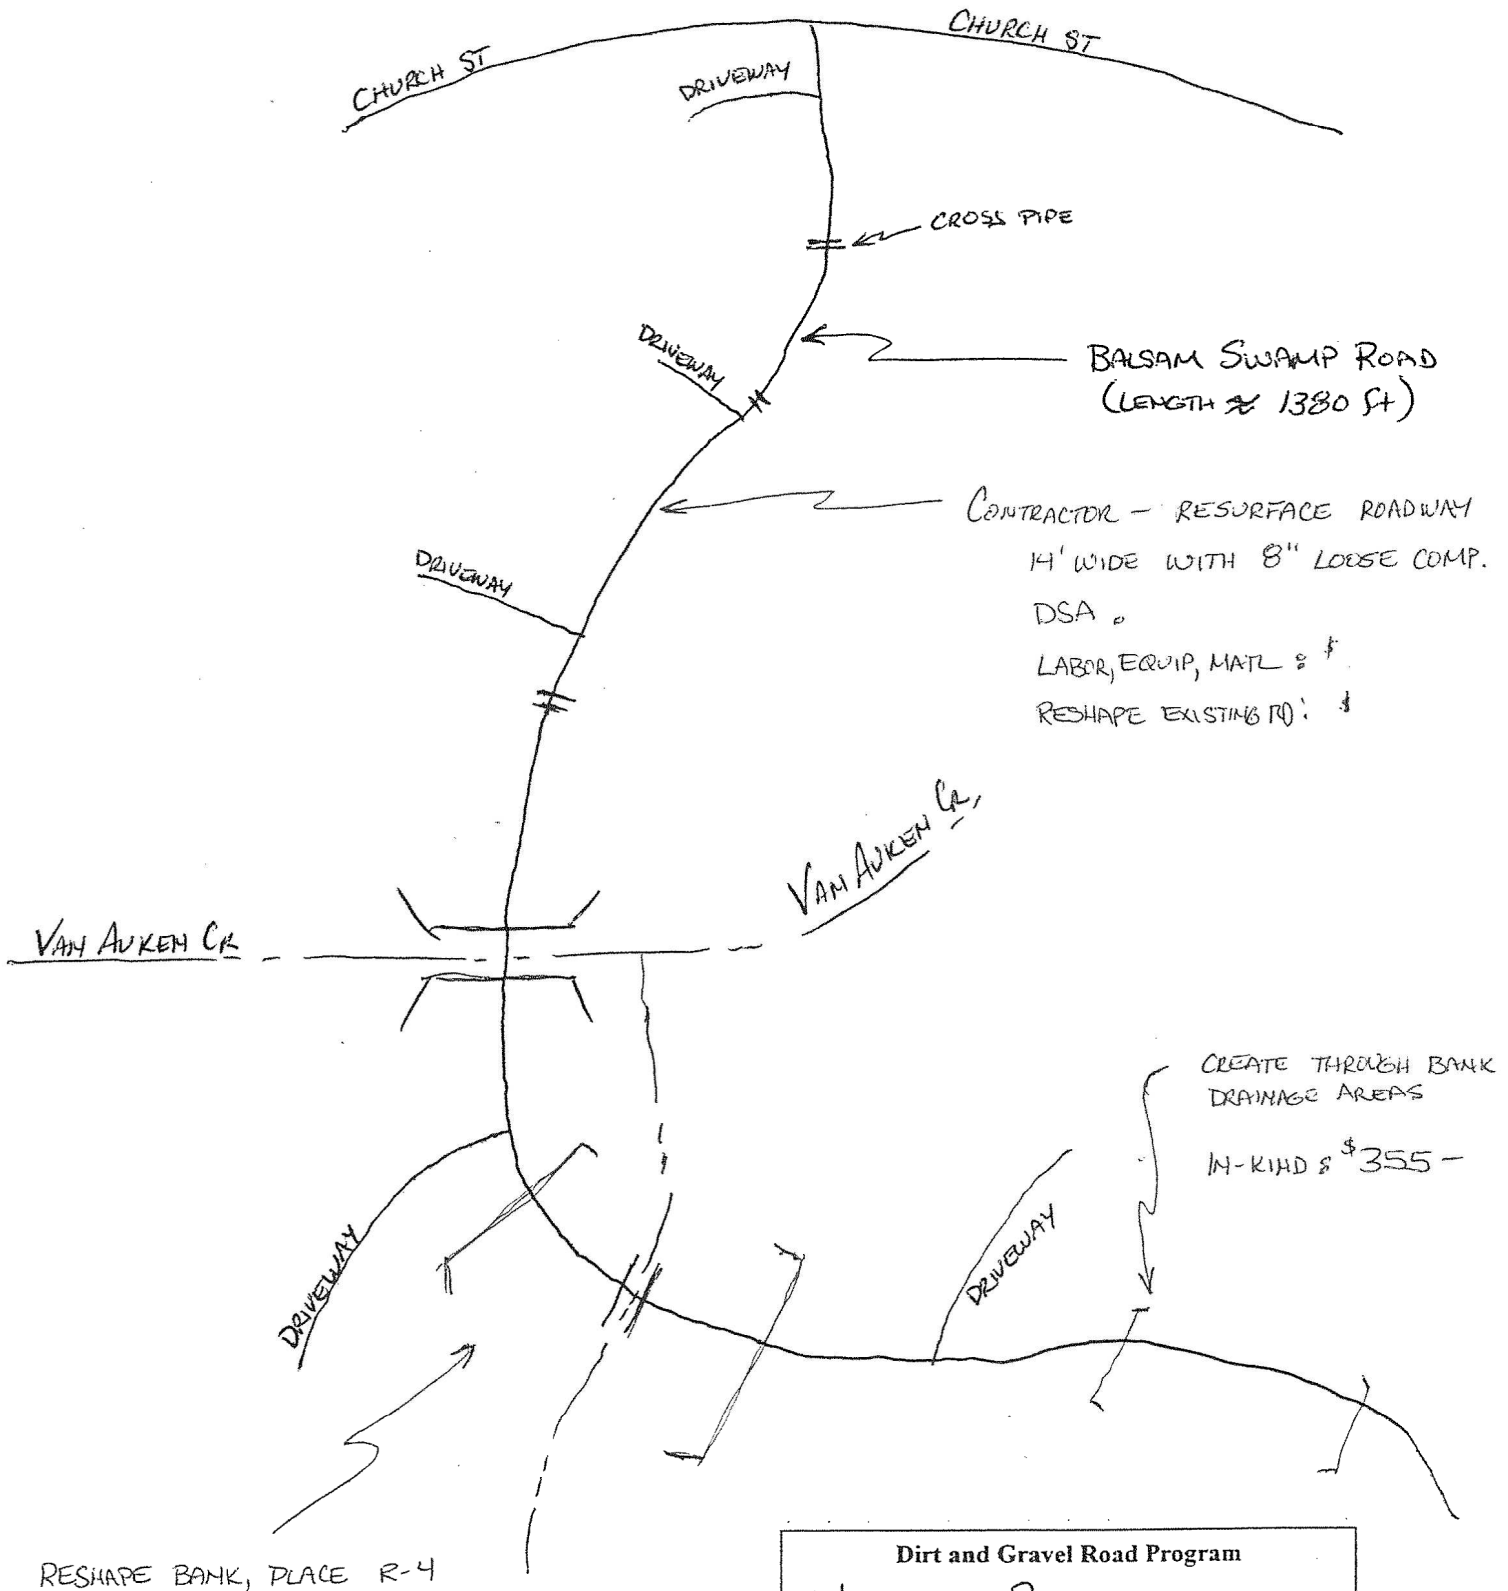

RESHAPE BANK, PLACE R-4

CONTRACTOR: LABOR, EQUIP, MATL: \$

IN-KIND: LABOR, EQUIP: 850-

Dirt and Gravel Road Program		
WAYNE County	PROMPTON Township	App #
scale	data	
